




**MANCHESTER BRIDGE  
DESIGN-BUILD  
INDUSTRY MEETING  
JANUARY 8, 2013**

# Project Team

- Susan Barry, Project Director
- Brian Burger, Deputy Project Director
- James Martin
- Mike Landvik
- Kevin Irving, FHWA

# Aerial view

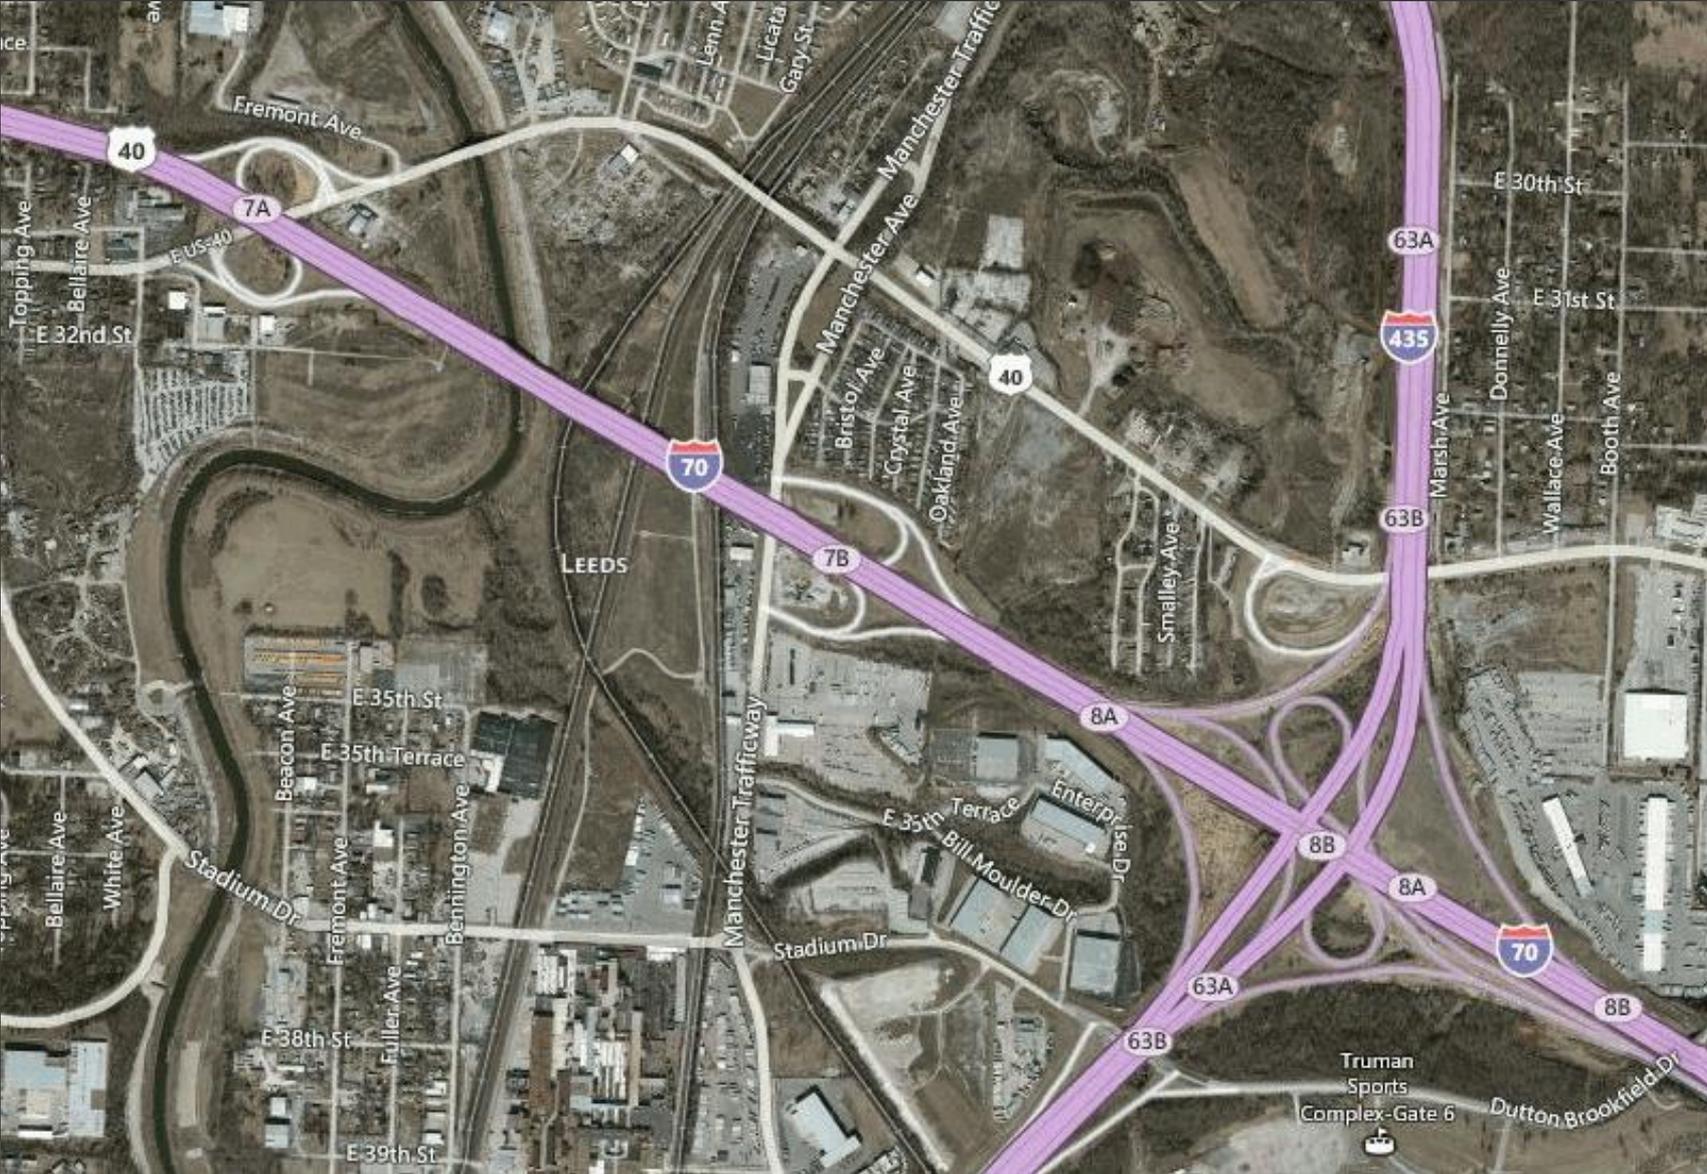

# Project Description

- Rehabilitation/reconstruction of the twin bridges (L0967) on I-70
- Reconstruction of historic Blue River bridge (J0526) on US 40
- Minimal impacts to traffic
- Potential additional scope

# Project Goals

1. Impress our customers through innovative solutions that conveniently and efficiently move drivers through the project during and after construction.
2. Construct durable structures that minimize future maintenance impacts.
3. Balance regional mobility with total project cost to achieve optimal value.
4. Deliver the project no later than December 15, 2016.

# Design-Build Model

- Set goals
- Two phased procurement
- Confidential meetings
- Final proposals
- Evaluation / award

# Cost

- \$58.7 Million in STIP for conventional construction methods
- Balance mobility with cost

# Flexibility

- Additional Applicable Standards (AAS)
- Quality Management plan
- Utility coordination
- Safety plan
- Co-location Contractor/MoDOT team

# Risk Allocation

MoDOT is proactively working on these risk items:

- Acquisition of temporary construction easements
- Utility relocation
- Third party agreements
- Railroad grade separation agreements
- Beazer RCRA site
- Historic Blue River bridge

# Aerial view



# Procurement Schedule

Item	Date
Issue RFQ	January 8, 2013
Deadline for submitting RFQ questions	January 21, 2013 (2:00 pm CST)
Final responses to questions posted & Final RFQ Addendum issued	January 25, 2013
SOQ due	February 8, 2013 (2:00 pm CST)
MoDOT notifies short-listed Submitters	February 22, 2013
Issue RFP	February 26, 2013
Final Proposal and Price Allocation due	Early June 2013

# Disadvantaged Business Enterprise

- 12% for construction activities
- 18% for design/professional services
- DBE firms must be certified with the Missouri Regional Certification Committee (MRCC)  
[http://www.modot.mo.gov/business/contractor\\_resources/External\\_Civil\\_Rights/DBE\\_program.htm](http://www.modot.mo.gov/business/contractor_resources/External_Civil_Rights/DBE_program.htm)

# Workforce goals

- ⦿ Federal workforce goals apply to project
  - 12.7% minority
  - 6.9% female
- ⦿ Goals apply per craft
- ⦿ On-The-Job training goals will apply if workforce goals aren't met per craft.

# Project Contacts

- Project Director – Susan Barry

ManchesterBridge@modot.mo.gov

816-607-2206

- External Civil Rights Director - Lester Woods

Lester.WoodsJr@modot.mo.gov

573-751-2859

[www.modot.org/ManchesterBridge](http://www.modot.org/ManchesterBridge)

# Questions???

